


Schedule Template




Schedule Template: New Home Construction


Gantt View Calendar View Task View Hypothetical Start: 8/3/2017 Thu

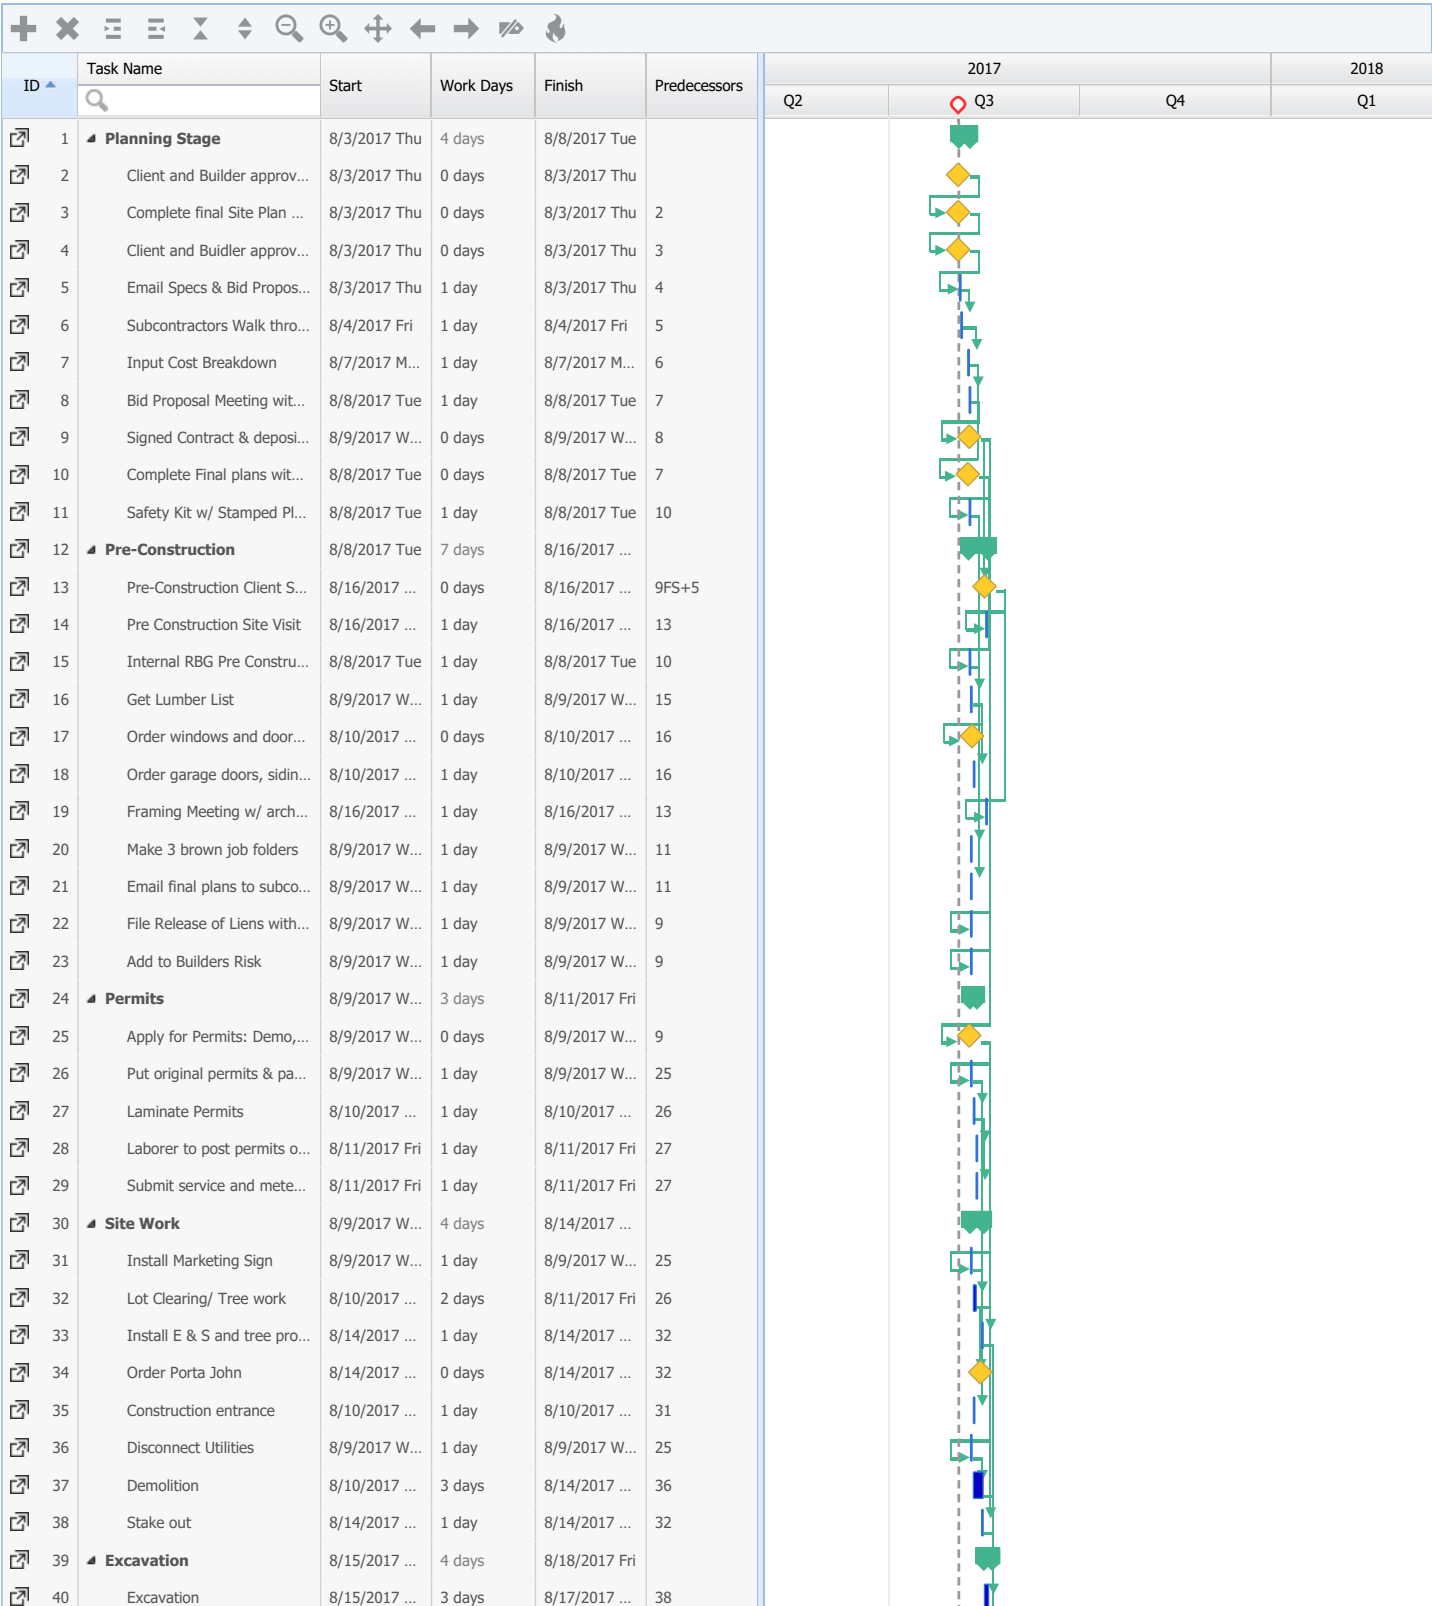


41	Order Steel	8/15/2017 ...	0 days	8/15/2017 ...	37
42	Order lumber for 1st Floo...	8/18/2017 Fri	0 days	8/18/2017 Fri	40
44	Order Exterior Columns	8/18/2017 Fri	0 days	8/18/2017 Fri	40
45	Foundation	8/15/2017 ...	17 days	9/6/2017 W...	
46	Form Footings	8/18/2017 Fri	1 day	8/18/2017 Fri	40
47	Inspect footings	8/18/2017 Fri	0 days	8/18/2017 Fri	40
48	Pour Footings	8/18/2017 Fri	0 days	8/18/2017 Fri	40
49	Install drain tile, stone a...	8/21/2017 ...	1 day	8/21/2017 ...	46
50	Form foundation	8/22/2017 ...	2 days	8/23/2017 ...	49
51	Inspect Foundation (not i...	8/24/2017 ...	0 days	8/24/2017 ...	50
52	Pour Foundation	8/24/2017 ...	1 day	8/24/2017 ...	51
53	Order dumpster	8/15/2017 ...	0 days	8/15/2017 ...	41
54	Water proof foundation	8/28/2017 ...	1 day	8/28/2017 ...	52FS+1
55	Set Steel	8/29/2017 ...	1 day	8/29/2017 ...	54
56	Exterior Selection Meetin...	8/21/2017 ...	1 day	8/21/2017 ...	46
57	Put first floor deck on	8/29/2017 ...	2 days	8/30/2017 ...	54
58	Order Draw 2	8/31/2017 ...	1 day	8/31/2017 ...	57
59	Rec'd Draw 2	9/1/2017 Fri	1 day	9/1/2017 Fri	58
60	Order rest of lumber	8/25/2017 Fri	1 day	8/25/2017 Fri	52
61	Back fill inspection	8/30/2017 ...	1 day	8/30/2017 ...	57FS-1
62	Backfill	8/31/2017 ...	1 day	8/31/2017 ...	61
63	Install rough-in plumbing...	9/1/2017 Fri	1 day	9/1/2017 Fri	62
64	Rough basement plumbi...	9/1/2017 Fri	1 day	9/1/2017 Fri	62
65	Slab Inspection	9/4/2017 M...	1 day	9/4/2017 M...	64
66	Pour basement slab	9/5/2017 Tue	2 days	9/6/2017 W...	65
67	Get Electrical & Plumbing...	8/15/2017 ...	1 day	8/15/2017 ...	33
68	Framing	9/1/2017 Fri	19 days	9/27/2017 ...	
69	Framing and call in colu...	9/1/2017 Fri	14 days	9/20/2017 ...	62
70	Order Draw 3	9/21/2017 ...	1 day	9/21/2017 ...	69
71	Rec'd Draw 3	9/22/2017 Fri	1 day	9/22/2017 Fri	70
72	Deliver Trusses	9/13/2017 ...	1 day	9/13/2017 ...	69FS-6
73	Deliver Windows	9/12/2017 ...	1 day	9/12/2017 ...	72FS-2
74	Install exterior columns	9/7/2017 Thu	1 day	9/7/2017 Thu	66
75	Order stairs	9/12/2017 ...	1 day	9/12/2017 ...	69FS-7
76	Install windows & doors	9/21/2017 ...	1 day	9/21/2017 ...	69
77	Roof installed	9/21/2017 ...	3 days	9/25/2017 ...	69
78	Install electric service	9/11/2017 ...	1 day	9/11/2017 ...	87
79	Order Draw 4	9/26/2017 ...	1 day	9/26/2017 ...	77
80	Rec'd Draw 4	9/27/2017 ...	1 day	9/27/2017 ...	79
81	Call Tyvek Rep: Waz to c...	9/26/2017 ...	1 day	9/26/2017 ...	77
82	Meeting 3 Electrical and ...	9/21/2017 ...	1 day	9/21/2017 ...	69
83	Layout kitchen & bathroo...	9/21/2017 ...	1 day	9/21/2017 ...	69
84	Inspect Concrete slabs	9/21/2017 ...	1 day	9/21/2017 ...	69
85	Pour garage & porch slabs	9/22/2017 Fri	1 day	9/22/2017 Fri	84
86	Water & Sewer	9/7/2017 Thu	4 days	9/12/2017 ...	
87	Drill Well	9/7/2017 Thu	2 days	9/8/2017 Fri	66
88	Install septic system	9/11/2017 ...	2 days	9/12/2017 ...	87
89	Stormwater Management	9/25/2017 ...	4 days	9/28/2017 ...	
90	Stormwater Management	9/25/2017 ...	4 days	9/28/2017 ...	85
91	Rough-In Mechanicals	8/18/2017 Fri	41 days	10/13/2017...	



92	Tie in water and sewer/s...	9/11/2017 ...	1 day	9/11/2017 ...	87
93	Rough-in plumbing	9/26/2017 ...	5 days	10/2/2017 ...	77
94	Rough-in HVAC	9/28/2017 ...	5 days	10/4/2017 ...	93FS-3
95	Rough-in Electrical	10/3/2017 ...	5 days	10/9/2017 ...	94FS-2
96	Rough-in Fireplace	10/3/2017 ...	1 day	10/3/2017 ...	93
97	Electrical Inspection	10/10/2017...	1 day	10/10/2017...	95
98	Rough-in audio/video/ala...	10/10/2017...	2 days	10/11/2017...	95
99	Frame soffits	10/12/2017...	1 day	10/12/2017...	98
100	Behind the wall clean ho...	10/10/2017...	0 days	10/10/2017...	95
101	Fire Stopping	10/10/2017...	1 day	10/10/2017...	100
102	Rough framing and mech...	10/11/2017...	1 day	10/11/2017...	101
103	Order draw 5	10/12/2017...	1 day	10/12/2017...	102
104	Rec'd Draw 5	10/13/2017...	1 day	10/13/2017...	103
105	call Drywall sub to walk s...	10/10/2017...	1 day	10/10/2017...	95
106	PECO Trench date for ele...	8/18/2017 Fri	0 days	8/18/2017 Fri	44
107	Call Comcast & Verizon, ...	9/12/2017 ...	1 day	9/12/2017 ...	78
108	Exterior Finishes	10/5/2017 ...	18 days	10/30/2017...	
109	Siding & Trim	10/5/2017 ...	5 days	10/11/2017...	93FS+2
110	Stucco	10/10/2017...	7 days	10/18/2017...	109FS-2
111	Stone	10/13/2017...	10 days	10/26/2017...	110FS-4
112	Shutters & Accents	10/27/2017...	1 day	10/27/2017...	111
113	Gutters & Downspouts	10/30/2017...	1 day	10/30/2017...	112
114	Install garage doors	10/19/2017...	1 day	10/19/2017...	93FS+12
115	Homeowner Pre-Close in...	10/10/2017...	1 day	10/10/2017...	
116	Homeowner Pre-Close in ...	10/10/2017...	1 day	10/10/2017...	100
117	Insulation	10/12/2017...	2 days	10/13/2017...	
118	Insulation	10/12/2017...	2 days	10/13/2017...	102
119	Insulation inspection	10/13/2017...	0 days	10/13/2017...	118FS-1
120	Meeting 4 with Client (In...	10/13/2017...	1 day	10/13/2017...	119
121	Order Interior Finishes	10/12/2017...	1 day	10/12/2017...	
122	Order Cabinetry	10/12/2017...	1 day	10/12/2017...	102
123	Select granite	10/12/2017...	1 day	10/12/2017...	102
124	Order Flooring	10/12/2017...	1 day	10/12/2017...	102
125	Order Light Fixtures	10/12/2017...	1 day	10/12/2017...	102
126	Order Plumbing Fixtures	10/12/2017...	1 day	10/12/2017...	102
127	Drywall	10/13/2017...	12 days	10/30/2017...	
128	Drywall	10/13/2017...	10 days	10/26/2017...	119
129	Drywall Inspection	10/17/2017...	1 day	10/17/2017...	128FS-8
130	Order Draw 6	10/27/2017...	1 day	10/27/2017...	128
131	Rec'd Draw 6	10/30/2017...	1 day	10/30/2017...	130
132	Call Mike Mackie to meas...	10/18/2017...	1 day	10/18/2017...	129
133	Exterior Site finishes	10/10/2017...	43 days	12/8/2017 Fri	
134	Exterior Walks	10/27/2017...	4 days	11/1/2017 ...	128
135	Bury propane tank	10/10/2017...	1 day	10/10/2017...	100
136	Base Coat paving	11/2/2017 ...	2 days	11/3/2017 Fri	134
137	Install Patios and decks	10/27/2017...	3 days	10/31/2017...	128
138	Retaining walls	10/27/2017...	4 days	11/1/2017 ...	128
139	Final grade	12/1/2017 Fri	2 days	12/4/2017 ...	138FS+20
140	Rake and Seed	12/5/2017 ...	2 days	12/6/2017 ...	139
141	Top coat driveway	12/5/2017 ...	1 day	12/5/2017 ...	139
142	Landscape packages	12/7/2017 ...	2 days	12/8/2017 Fri	140

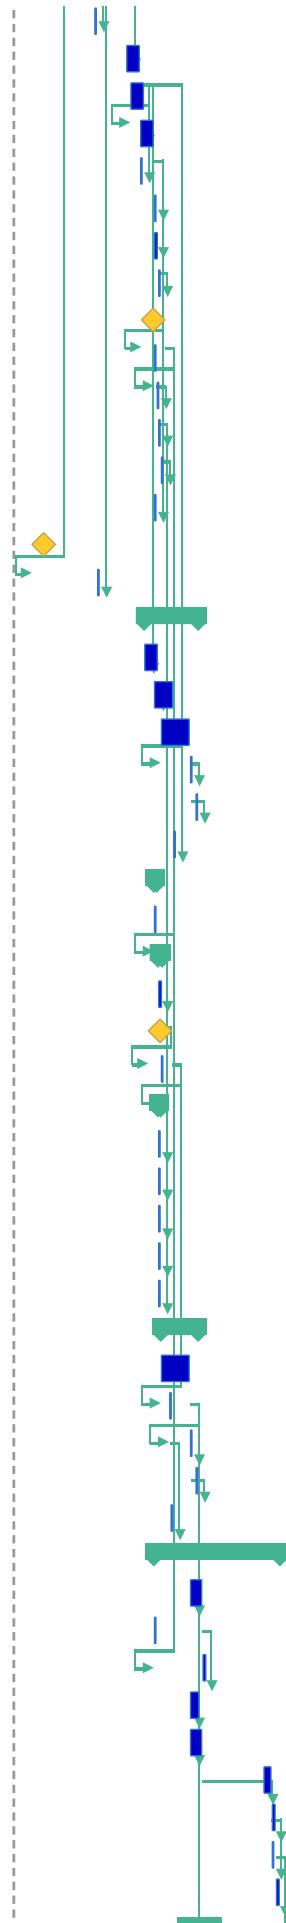

143	▲ Trim	10/25/2017...	9 days	11/6/2017 ...	
144	Trim Delivery	10/25/2017...	0 days	10/25/2017...	128FS-2
145	Trim installation	10/27/2017...	6 days	11/3/2017 Fri	128
146	Install Railings	11/3/2017 Fri	2 days	11/6/2017 ...	145FS-1
147	Rough paint clean	11/6/2017 ...	1 day	11/6/2017 ...	145
148	Fireplace mantle and fac...	10/27/2017...	1 day	10/27/2017...	144FS+2
149	▲ Paint	11/7/2017 ...	4 days	11/10/2017...	
150	Paint - Interior, including...	11/7/2017 ...	3 days	11/9/2017 ...	147
151	Paint - Exterior	11/10/2017...	1 day	11/10/2017...	150
152	Order Draw 7	11/10/2017...	0 days	11/10/2017...	150
153	Rec'd Draw 7	11/14/2017...	0 days	11/14/2017...	152FS+2
154	▲ Flooring	11/10/2017...	13 days	11/29/2017...	
155	Tile Installation	11/10/2017...	6 days	11/17/2017...	150
156	Hardwood-install, stain a...	11/20/2017...	7 days	11/29/2017...	155
157	Order shower door	11/20/2017...	1 day	11/20/2017...	155
158	Order Bath Accessories &...	11/21/2017...	1 day	11/21/2017...	157
159	▲ Interior Finishes	11/17/2017...	18 days	12/13/2017...	
160	Cabinetry & Vanity delivery	11/30/2017...	1 day	11/30/2017...	156
161	Cabinetry installation	11/17/2017...	3 days	11/21/2017...	155FS-1
162	Cabinetry Hardware insta...	11/21/2017...	0 days	11/21/2017...	161FS-1
163	Appliance delivery	12/1/2017 Fri	1 day	12/1/2017 Fri	160
164	Granite template	11/22/2017...	1 day	11/22/2017...	161
165	Countertop installation	11/30/2017...	1 day	11/30/2017...	164FS+4
166	Appliance installation	12/1/2017 Fri	1 day	12/1/2017 Fri	165
167	Backsplash installation	12/4/2017 ...	2 days	12/5/2017 ...	166
168	Trim Final- shoe molding ...	11/22/2017...	1 day	11/22/2017...	161
169	Finish HVAC	11/22/2017...	2 days	11/24/2017...	161
170	Finish plumbing	11/27/2017...	2 days	11/28/2017...	169
171	Finish electric, Cable/Pho...	11/29/2017...	2 days	11/30/2017...	170
172	Order Draw 8	12/1/2017 Fri	1 day	12/1/2017 Fri	171
173	Rec'd Draw 8	12/4/2017 ...	1 day	12/4/2017 ...	172
174	Fireplace Start Up	11/24/2017...	1 day	11/24/2017...	164
175	Finish security/audio	11/27/2017...	1 day	11/27/2017...	169
176	Attic and basement insul...	11/27/2017...	2 days	11/28/2017...	169
177	Install shower doors	12/1/2017 Fri	1 day	12/1/2017 Fri	165
178	Drywall touch-ups	12/1/2017 Fri	2 days	12/4/2017 ...	171
179	Install Mailbox	12/5/2017 ...	1 day	12/5/2017 ...	178
180	Interior pre-carpet cleani...	12/5/2017 ...	1 day	12/5/2017 ...	178
181	Carpet installation	12/5/2017 ...	1 day	12/5/2017 ...	178
182	Final Paint	12/6/2017 ...	4 days	12/11/2017...	181
183	Final Poly coat	12/12/2017...	1 day	12/12/2017...	182
184	As Built	12/7/2017 ...	1 day	12/7/2017 ...	140
185	Install shelving/mirrors/b...	12/13/2017...	1 day	12/13/2017...	183
186	▲ Final Clean	12/13/2017...	7 days	12/21/2017...	
187	Final Clean	12/13/2017...	4 days	12/18/2017...	183
188	U&O Inspection	12/15/2017...	1 day	12/15/2017...	183FS+2
189	Order Draw 9	12/18/2017...	1 day	12/18/2017...	188
190	Rec'd Draw 9	12/19/2017...	1 day	12/19/2017...	189
191	Settlement Punchlist	12/15/2017...	1 day	12/15/2017...	187FS-2
192	Punch Out List	12/18/2017...	4 days	12/21/2017...	191
193	Pull dumpster and Porta-...	12/15/2017...	1 day	12/15/2017...	187FS-2
194	▲ Walk Through	12/19/2017...	3 days	12/21/2017...	



195	Buyer Walk Through	12/19/2017...	1 day	12/19/2017...	187
196	Settlement	12/20/2017...	1 day	12/20/2017...	195
197	Remove from Warranty	12/21/2017...	1 day	12/21/2017...	186
198	Move to Warranty in QB, ...	12/20/2017...	1 day	12/20/2017...	195
199	Send contractor list & we...	12/20/2017...	1 day	12/20/2017...	195
200	Send survey	12/21/2017...	1 day	12/21/2017...	199

Save Template & Keep Editing

Save Template & Exit

Cancel Changes & Exit

Copyright 2005-2017 Co-construct, LLC. All rights reserved.
