



Schedule Template




Schedule Template: KB: Portfolio Home on Basement

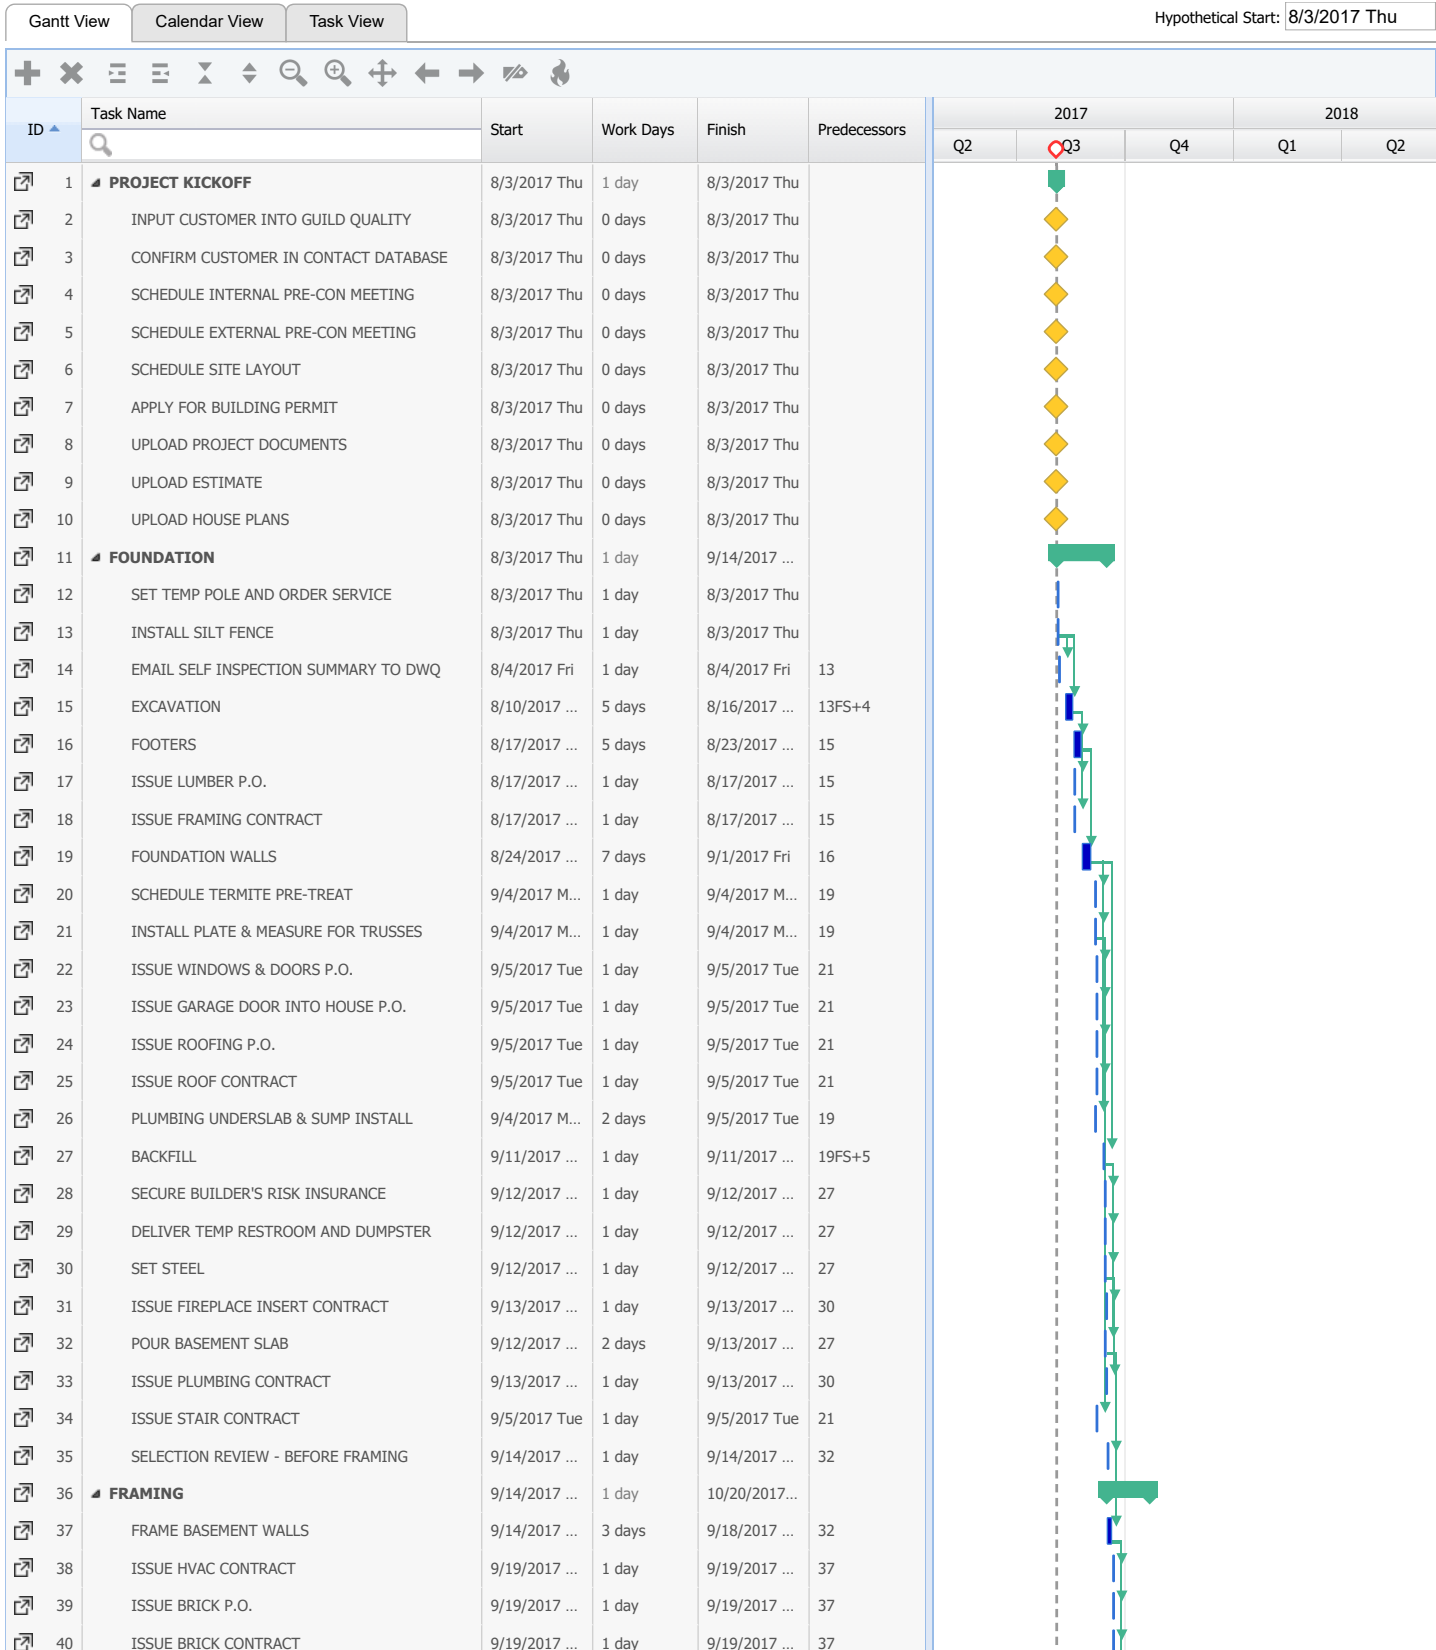


41	DELIVER TEMP STAIRS	9/19/2017 ...	1 day	9/19/2017 ...	37
42	FRAME 1ST FLOOR & GARAGE	9/19/2017 ...	5 days	9/25/2017 ...	37
44	ISSUE SIDING P.O.	10/3/2017 ...	1 day	10/3/2017 ...	43
45	ISSUE SIDING CONTRACT	10/3/2017 ...	1 day	10/3/2017 ...	43
46	ISSUE ELECTRIC CONTRACT	9/26/2017 ...	1 day	9/26/2017 ...	42
47	ISSUE LOW VOLT CONTRACT	10/9/2017 ...	1 day	10/9/2017 ...	43FS+4
48	ISSUE SECURITY CONTRACT	10/10/2017...	1 day	10/10/2017...	47
49	FRAME ROOF SYSTEM	10/3/2017 ...	10 days	10/16/2017...	43
50	ISSUE INSULATION CONTRACT	10/16/2017...	1 day	10/16/2017...	47FS+4
51	ISSUE GUTTERS & COLUMNS CONTRACT	10/17/2017...	1 day	10/17/2017...	50
52	ISSUE DRYWALL CONTRACT	10/17/2017...	1 day	10/17/2017...	49
53	SET WINDOWS & DOORS	10/17/2017...	2 days	10/18/2017...	49
54	PRE-ROUGH WALKTHROUGHS	10/19/2017...	0 days	10/19/2017...	53
55	SELECTION REVIEW - BEFORE ROUGH-INS	10/19/2017...	1 day	10/19/2017...	53
56	LAYOUT CABINETS	10/19/2017...	0 days	10/19/2017...	53
57	SHINGLES INSTALLED	10/18/2017...	3 days	10/20/2017...	49FS+1
58	ROUGH-INS	10/19/2017...	1 day	11/23/2017...	
59	SET FIREPLACE INSERTS	10/23/2017...	1 day	10/23/2017...	57
60	PLUMBING ROUGH-IN	10/24/2017...	5 days	10/30/2017...	54FS+3
61	CONFIRM WATER SERVICE INSTALLED	10/19/2017...	1 day	10/19/2017...	54
62	ORDER GAS SERVICE LINE	10/19/2017...	1 day	10/19/2017...	54
63	HVAC ROUGH-IN	10/27/2017...	5 days	11/2/2017 ...	54FS+6
64	ISSUE CABINET CONTRACT	10/31/2017...	1 day	10/31/2017...	60
65	SET FINISHED STAIRS	11/3/2017 Fri	1 day	11/3/2017 Fri	63
66	LIGHTING AND LOW VOLTAGE WALKTHROUGH	11/2/2017 ...	1 day	11/2/2017 ...	54FS+10
67	SECURITY ROUGH-IN	11/3/2017 Fri	2 days	11/6/2017 ...	63
68	ELECTRIC ROUGH-IN	11/3/2017 Fri	5 days	11/9/2017 ...	63
69	ISSUE OVERHEAD DOOR CONTRACT	11/3/2017 Fri	1 day	11/3/2017 Fri	63
70	ISSUE WOOD FLOORING CONTRACT	11/3/2017 Fri	1 day	11/3/2017 Fri	63
71	ISSUE TILE P.O.	11/3/2017 Fri	1 day	11/3/2017 Fri	63
72	ISSUE TILE CONTRACT	11/3/2017 Fri	1 day	11/3/2017 Fri	63
73	TRIM SUPPLIER WALKTHROUGH	11/13/2017...	1 day	11/13/2017...	68FS+1
74	ISSUE TRIM P.O.	11/14/2017...	1 day	11/14/2017...	73
75	ISSUE TRIM CONTRACT	11/14/2017...	1 day	11/14/2017...	73
76	BUILD ELECTRIC SERVICE AND ORDER T.O.P.	11/10/2017...	1 day	11/10/2017...	68
77	LOW VOLTAGE ROUGH-IN	11/10/2017...	2 days	11/13/2017...	68
78	CENTRAL VAC ROUGH-IN	11/10/2017...	2 days	11/13/2017...	68
79	FRAMING INSPECTION PASSED	11/17/2017...	1 day	11/17/2017...	68FS+5
80	ENERGY RATING FRAMING REVIEW	11/14/2017...	1 day	11/14/2017...	78
81	INSULATE WALLS	11/20/2017...	3 days	11/22/2017...	79
82	ISSUE BUILT-IN CONTRACT	11/23/2017...	1 day	11/23/2017...	81
83	ISSUE COUNTERTOP CONTRACT	11/23/2017...	1 day	11/23/2017...	81
84	ISSUE LIGHTING P.O.	11/23/2017...	1 day	11/23/2017...	81
85	DRYWALL & TRIM	11/23/2017...	1 day	1/5/2018 Fri	
86	HANG & FINISH DRYWALL	11/23/2017...	15 days	12/13/2017...	81
87	ISSUE APPLIANCES CONTRACT	12/14/2017...	1 day	12/14/2017...	86
88	TRIM AND BUILT-IN REVIEW WITH OWNER	12/14/2017...	1 day	12/14/2017...	86
89	ORDER ATTIC ACCESS LADDER	12/14/2017...	1 day	12/14/2017...	86
90	INSTALL GARAGE DOOR INTO HOUSE	12/14/2017...	1 day	12/14/2017...	86
91	FIREPLACE SURROUND(S) INSTALLED	12/14/2017...	1 day	12/14/2017...	86



92	REGISTERS AND GRILLS INSTALLED	12/14/2017...	1 day	12/14/2017...	86
93	INSTALL HOGS HAIR ON AIR RETURNS	12/15/2017...	1 day	12/15/2017...	92
94	GARAGE DOORS SET	12/14/2017...	1 day	12/14/2017...	86
95	LAY UNFINISHED FLOOR	12/14/2017...	2 days	12/15/2017...	86
96	SELECTION REVIEW - BEFORE TRIM	12/18/2017...	1 day	12/18/2017...	95
97	BULLNOSE DELIVERED FOR HARDWOOD	12/14/2017...	1 day	12/14/2017...	86
98	LAY TILE FLOORS & SHOWER	12/14/2017...	5 days	12/20/2017...	86
99	ISSUE PAINT CONTRACT	12/21/2017...	1 day	12/21/2017...	98
100	FINISH TRIM INSTALL	12/20/2017...	10 days	1/2/2018 Tue	95FS+2
101	CABINETS INSTALL	12/21/2017...	3 days	12/25/2017...	98
102	BUILT-INS INSTALL	1/3/2018 W...	3 days	1/5/2018 Fri	100
103	INSTALL COUNTERTOPS	1/2/2018 Tue	1 day	1/2/2018 Tue	101FS+5
104	INSTALL KITCHEN BACKSPLASH	1/3/2018 W...	2 days	1/4/2018 Thu	103
105	EXTERIOR FINISHES	10/19/2017...	1 day	12/5/2017 ...	
106	LAY BRICK VENEER	10/19/2017...	10 days	11/1/2017 ...	53
107	CLEAN BRICK AND SPREAD STRAW	11/2/2017 ...	2 days	11/3/2017 Fri	106
108	INSTALL COPPER COUNTERFLASHING	11/6/2017 ...	1 day	11/6/2017 ...	107
109	INSTALL WINDOW WELLS	11/2/2017 ...	2 days	11/3/2017 Fri	106
110	INSTALL SOFFIT, FASCIA, AND SIDING	11/6/2017 ...	5 days	11/10/2017...	106FS+2
111	INSTALL & ACTIVATE EXTERIOR LIGHTS	11/13/2017...	1 day	11/13/2017...	110
112	INSTALL CHIMNEY CAP	11/13/2017...	1 day	11/13/2017...	110
113	INSTALL COLUMNS AND SHUTTERS	11/13/2017...	2 days	11/14/2017...	110
114	INSTALL GUTTERS	11/15/2017...	2 days	11/16/2017...	110FS+2
115	POUR PORCH SLABS	11/6/2017 ...	1 day	11/6/2017 ...	106FS+2
116	POUR GARAGE SLAB	11/6/2017 ...	1 day	11/6/2017 ...	106FS+2
117	POUR SIDEWALKS AND DRIVEWAY	11/15/2017...	3 days	11/17/2017...	110FS+2
118	PORCH AND WALK PAVERS	11/22/2017...	3 days	11/24/2017...	117FS+2
119	ROUGH FINISH GRADE AND HVAC PADS	11/27/2017...	1 day	11/27/2017...	118
120	LANDSCAPE AND STREET TREES	11/27/2017...	2 days	11/28/2017...	118
121	INSTALL MAILBOX	11/27/2017...	1 day	11/27/2017...	118
122	LAY SOD	12/1/2017 Fri	2 days	12/4/2017 ...	120FS+2
123	CONFIRM SPLASH BLOCKS ARE IN PLACE	12/5/2017 ...	1 day	12/5/2017 ...	122
124	INTERIOR FINISHES	1/3/2018 W...	1 day	2/16/2018 Fri	
125	FINISH PLUMBING FIXTURES	1/3/2018 W...	7 days	1/11/2018 ...	103
126	ISSUE CARPET CONTRACT	1/12/2018 Fri	1 day	1/12/2018 Fri	125
127	FINISH ELECTRIC AND LIGHTING	1/5/2018 Fri	7 days	1/15/2018 ...	104
128	FINISH HVAC	1/16/2018 ...	2 days	1/17/2018 ...	127
129	FIRST (2) COATS ON WOOD FLOORS	1/16/2018 ...	4 days	1/19/2018 Fri	127
130	INSTALL SHOEMOLD	1/22/2018 ...	1 day	1/22/2018 ...	129
131	PHASE (1) CLEANING BEFORE HARDWOOD FINI...	1/16/2018 ...	1 day	1/16/2018 ...	127
132	PREFINISHED WOOD FLOORS	1/16/2018 ...	3 days	1/18/2018 ...	127
133	INSTALL APPLIANCES	1/22/2018 ...	2 days	1/23/2018 ...	129
134	PHASE 2 CLEANING BEFORE PAINT STARTS	1/24/2018 ...	1 day	1/24/2018 ...	133
135	PRESENT LANDSCAPING PLAN TO HOMEOWNER	1/25/2018 ...	1 day	1/25/2018 ...	134
136	5 WEEKS FROM CLOSE OWNER MEETING	1/25/2018 ...	1 day	1/25/2018 ...	134
137	INTERIOR PAINT	1/29/2018 ...	15 days	2/16/2018 Fri	136FS+1
138	CLOSEOUT TASKS	2/19/2018 ...	1 day	3/13/2018 ...	
139	PLATE OUT LOW VOLTAGE	2/19/2018 ...	2 days	2/20/2018 ...	137
140	CABINET PUNCH	2/19/2018 ...	1 day	2/19/2018 ...	137
141	CONFIRM DANNY SCHEDULED FOR TWO WEEK	2/19/2018 ...	1 day	2/19/2018 ...	137
142	SET GAS LOGS	2/19/2018 ...	1 day	2/19/2018 ...	137

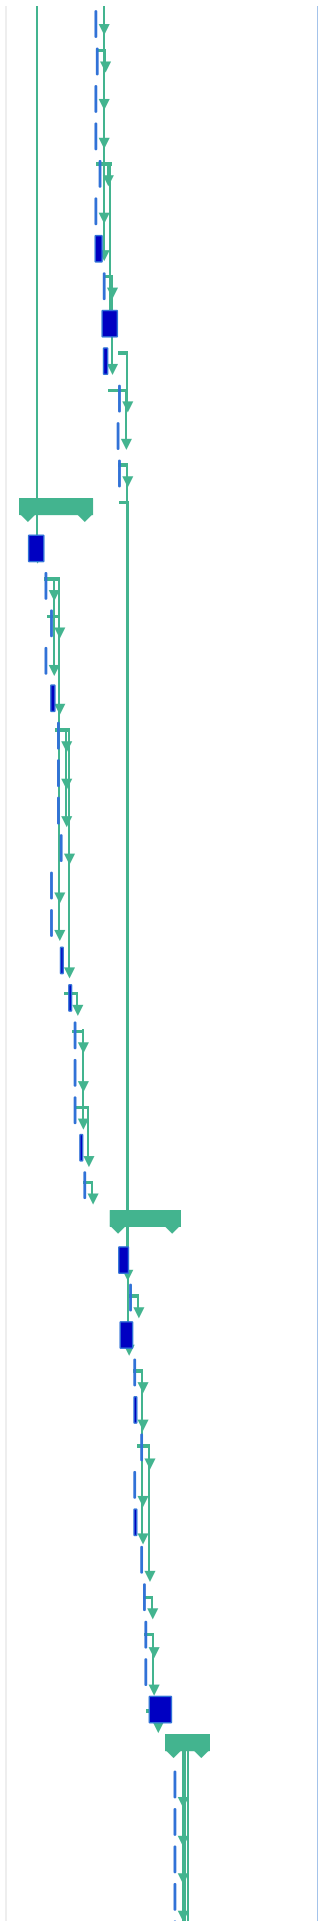

143	FINISH SECURITY SYSTEM	2/19/2018 ...	1 day	2/19/2018 ...	137
144	FINISH CENTRAL VAC	2/19/2018 ...	1 day	2/19/2018 ...	137
145	INSTALL MIRRORS, BATH ACCESSORIES, AND S...	2/19/2018 ...	2 days	2/20/2018 ...	137
146	INSTALL SHELVING	2/21/2018 ...	2 days	2/22/2018 ...	137FS+2
147	INSTALL FINISH DOOR HARDWARE	2/21/2018 ...	1 day	2/21/2018 ...	137FS+2
148	INSTALL CARPET	2/23/2018 Fri	3 days	2/27/2018 ...	137FS+4
149	HERS RATING COMPLETE	2/28/2018 ...	1 day	2/28/2018 ...	148
150	TWO WEEK FROM CLOSE OWNER MEETING	2/28/2018 ...	1 day	2/28/2018 ...	148
151	APPLIANCE ORIENTATION	2/28/2018 ...	1 day	2/28/2018 ...	148
152	HVAC ORIENTATION	2/28/2018 ...	1 day	2/28/2018 ...	148
153	CONFIRM DANNY SCHEDULED FOR PRE-CLOSE	3/1/2018 Thu	1 day	3/1/2018 Thu	150
154	APPLY FINISH COAT TO WOOD FLOORS	3/5/2018 M...	1 day	3/5/2018 M...	148FS+3
155	CERTIFICATE OF OCCUPENCY	2/28/2018 ...	1 day	2/28/2018 ...	148
156	FINAL CLEAN	3/6/2018 Tue	1 day	3/6/2018 Tue	154
157	PRE-CLOSE OWNER MEETING	3/7/2018 W...	1 day	3/7/2018 W...	156
158	SECURITY ORIENTATION	3/7/2018 W...	1 day	3/7/2018 W...	156
159	CENTRAL VAC ORIENTATION	3/7/2018 W...	1 day	3/7/2018 W...	156
160	PROJECT COMPLETE - MOVE IN	3/12/2018 ...	1 day	3/12/2018 ...	157FS+2
161	WALKTHROUGH MILESTONES IN WARRANTY A...	3/13/2018 ...	1 day	3/13/2018 ...	160

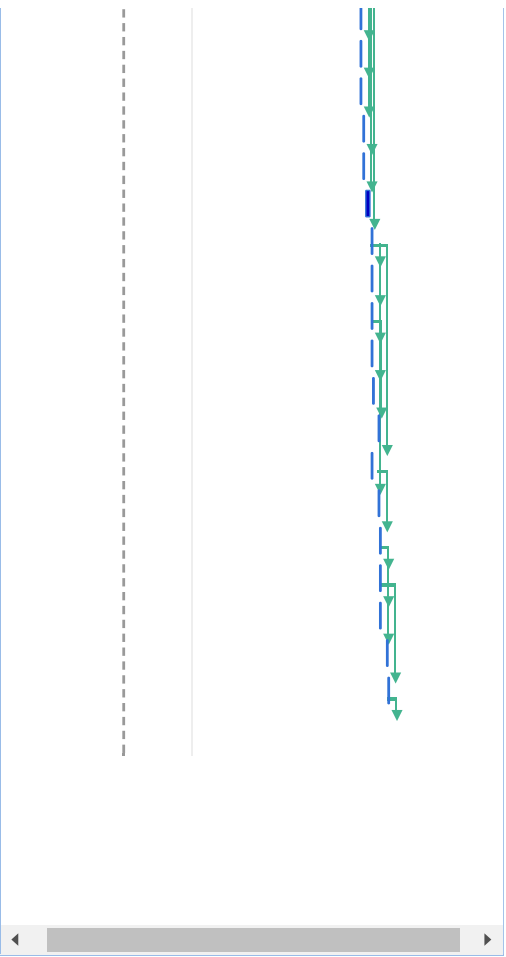

Save Template & Keep Editing

Save Template & Exit

[Cancel Changes & Exit](#)

Copyright 2005-2017 Co-construct, LLC. All rights reserved.
